



OAHU Pads Poured



Risers' installation in Herman Brown

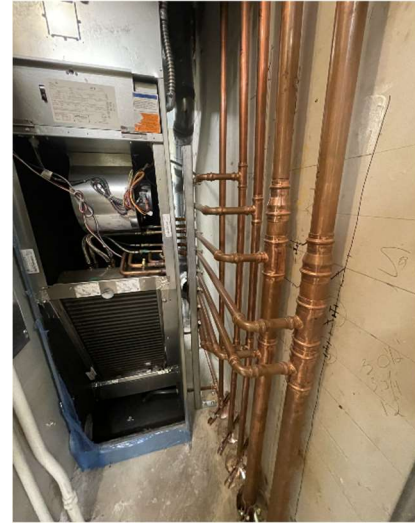

Installation of Subpanel Wiring

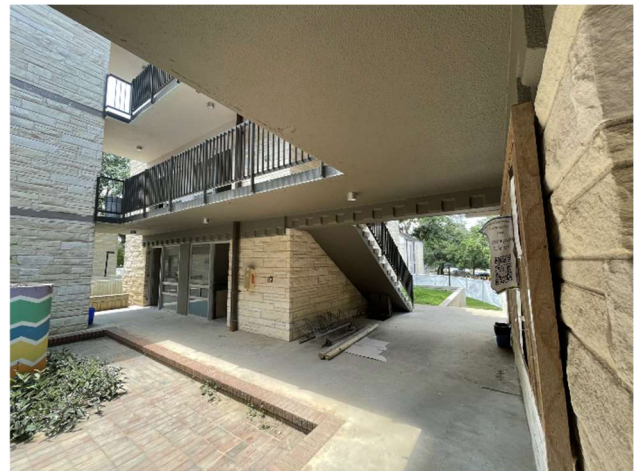

Painting Herman Brown Exterior

This Week's Activities:

- Continue install of subpanel components
- Continue installing carbon main pipe in crawlspace
- Start riser installation in Herman Brown
- Pour concrete for OAHU pad
- Start painting Herman Brown exterior ceiling

Upcoming Activities:

- OAHU delivered and set on pad
- Install subpanel components in Moody Shearn
- Performing pressure test on risers
- Install all mechanical and electrical components to OAHU
- Continue installing risers in Herman Brown

